



Migration playbook for AWS large migrations

AWS Prescriptive Guidance



AWS Prescriptive Guidance: Migration playbook for AWS large migrations

Copyright © 2026 Amazon Web Services, Inc. and/or its affiliates. All rights reserved.

Amazon's trademarks and trade dress may not be used in connection with any product or service that is not Amazon's, in any manner that is likely to cause confusion among customers, or in any manner that disparages or discredits Amazon. All other trademarks not owned by Amazon are the property of their respective owners, who may or may not be affiliated with, connected to, or sponsored by Amazon.

Table of Contents

Introduction	1
Guidance for large migrations	1
About the runbooks, tools, and templates	2
Attachments	3
Stage 1: Initializing a large migration	4
Task 1: Validating the migration patterns and metadata	4
Step 1: Validate the migration patterns	5
Step 2: Validate the migration metadata and wave plan	6
Task exit criteria	7
Task 2: Creating drafts of the migration runbooks	8
Step 1: Create a migration runbook draft for each pattern	8
Step 2: Update the migration runbooks with your policies and processes	9
Task exit criteria	10
Task 3: Analyzing and testing your migration runbooks	11
Step 1: Conduct a walkthrough of each runbook	11
Step 2: Conduct a POC that tests each migration pattern	11
Step 3: Review and identify the gaps in the current migration runbook drafts	12
Task exit criteria	12
Task 4: Improving your migration runbooks	12
Step 1: Update the migration runbooks and repeat the testing	13
Step 2: Automate repetitive tasks	13
Step 3: Build a migration task list	14
Task exit criteria	14
Stage 2: Implementing a large migration	16
Task 1: Performing sprint planning for scheduled waves	16
Step 1: Review the backlog for the scheduled waves	17
Step 2: Assign tasks and establish due dates	17
Task 2: Performing pre-migration and migration tasks	17
Task 3: Performing cutover tasks	18
Task 4: Reviewing and improving the migration runbooks	19
Step 1: Review the completed waves and identify gaps in the current migration runbook ...	19
Step 2: Update the migration runbooks and complete testing	20
Resources	21
AWS large migrations	21

Additional references 21

Contributors 22

Document history 23

Migration playbook for AWS large migrations

Wally Lu, Chris Baker, Tuhin Mukherjee, and Senay Swinney, Amazon Web Services

In a large migration, the migration workstream uses the wave plans and migration metadata supplied by the portfolio workstream in order to migrate workloads to the AWS Cloud. The migration workstream is responsible for submitting any change requests, migrating the application, coordinating application testing with the application owners, performing cutover, and monitoring the application through the hypercare period. In the first stage, initializing a large migration, you create the runbooks that the migration workstream uses to migrate the applications and servers. In the second stage, implementing a large migration, the migration workstream plans sprints and uses the migration runbooks in order to migrate and cutover the applications. For more information about core and supporting workstreams, see [Workstreams in a large migration](#) in the *Foundation playbook for AWS large migrations*.


This migration playbook outlines the tasks of the migration workstream, which spans both stages of a large migration, initialization and implementation:

- In stage 1, *initialize*, you draft, test, and refine the runbooks, and then you automate manual tasks for each migration pattern.
- In stage 2, *implement*, you perform the migration with the predefined runbooks built in stage 1.

Guidance for large migrations

Migrating 300 or more servers is considered a large migration. The people, process, and technology challenges of a large migration project are typically new to most enterprises. This document is part of an AWS Prescriptive Guidance series about large migrations to the AWS Cloud. This series is designed to help you apply the correct strategy and best practices from the outset, to streamline your journey to the cloud.

The following figure shows the other documents in this series. Review the strategy first, then the guides, and then proceed to the playbooks. To access the complete series, see [Large migrations to the AWS Cloud](#).

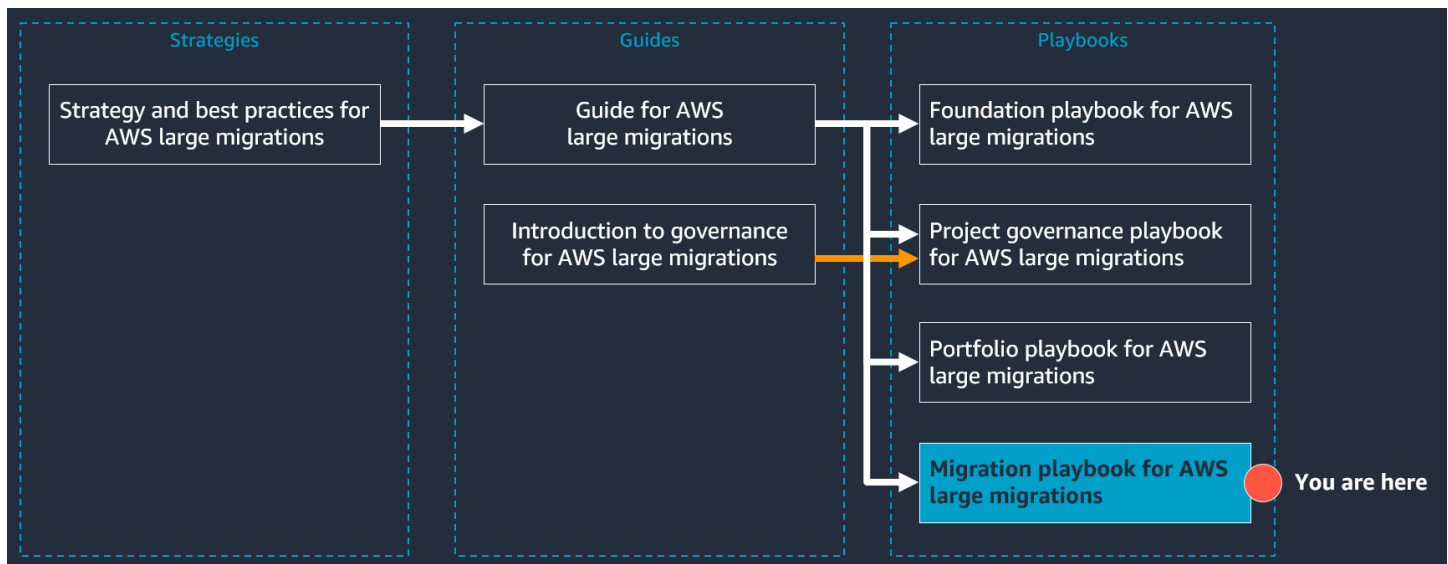

About the runbooks, tools, and templates

We recommend using the attached templates and then customizing them for your portfolio, processes, and environment. The provided templates include standard processes, typical cutover processes, and placeholders for processes that are unique to your environment. The instructions in this playbook tell you when and how to customize each of these templates. This playbook includes the following templates:

- Rehost migration runbook template
- Rehost migration task list template

For migration patterns, from which you can build your own runbooks, see [AWS Prescriptive Guidance migration patterns](#).

Migration runbooks require varying levels of detail:

- **Detailed runbooks** – Detailed runbooks are best suited for migration patterns that you will repeat many times. For these patterns, we recommend starting with the *Rehost migration runbook template* (Microsoft Word format). This template captures as many details as possible, including screenshots and step-by-step instructions, and it is designed to help multiple people perform the same task consistently.
- **Task List** – For migration patterns that are one-off or very simple, a short task list is a better option. For these patterns, we recommend starting with the *Rehost migration task list template* (Microsoft Excel format). This template contains a high-level task list and is typically used for

tracking and managing ownership of tasks. You can also use a task list to track the status of tasks that are documented in a runbook.

Whether you are using a detailed runbook or a short task list, verify that your runbook describes the tasks in sequence. For complex tasks, you can provide links to external documentation.

Attachments

To access additional content that is associated with this document, download and unzip the following file:

[attachment.zip](#)

Stage 1: Initializing a large migration

In the initialize stage, the goal is to define standard operating procedures (SOPs) for the large migration, also known as *runbooks*. You build custom runbooks based on your company's policies and processes. If another team member is responsible for defining the runbooks in your large migration project, skip to [Stage 2: Implementing a large migration](#), where you will use the runbooks to prioritize applications and perform wave planning. Stage 1 consists of the following tasks and steps:

- [Task 1: Validating the migration patterns and migration metadata](#)
 - [Step 1: Validate the migration patterns](#)
 - [Step 2: Validate the migration metadata and wave plan](#)
- [Task 2: Creating drafts of the migration runbooks](#)
 - [Step 1: Create a migration runbook draft for each pattern](#)
 - [Step 2: Update the migration runbooks with your policies and processes](#)
- [Task 3: Analyzing and testing your migration runbooks](#)
 - [Step 1: Conduct a walkthrough of each runbook](#)
 - [Step 2: Conduct a POC that tests each migration pattern](#)
 - [Step 3: Review and identify the gaps in the current migration runbook drafts](#)
- [Task 4: Improving your migration runbooks](#)
 - [Step 1: Update the migration runbooks and repeat the testing](#)
 - [Step 2: Automate repetitive tasks](#)
 - [Step 3: Build a migration task list](#)

With the migration runbooks in place, in stage 2, the migration teams follow the procedures and perform large migrations that have predictable and measurable outcomes.

Task 1: Validating the migration patterns and metadata

In this task, you validate the migration patterns identified in the assessment and wave planning activities in the portfolio workstream, and then you validate the migration metadata source. The goal is to verify that sufficient data has been collected to support each migration pattern.

This task consists of the following steps:

- [Step 1: Validate the migration patterns](#)
- [Step 2: Validate the migration metadata and wave plan](#)

Step 1: Validate the migration patterns

In the portfolio workstream, you performed an initial assessment of the application portfolio, selected migration strategies, and identified migration patterns for each strategy. This information should be contained in your portfolio assessment runbook. For more information, see the [Portfolio playbook for AWS large migrations](#).

In this step, you review the migration strategies, verify that you have identified all migration patterns, and confirm that you are ready to draft migration runbooks. You might repeat this task throughout the project, and as your understanding of the portfolio matures, it is likely you will identify additional migration patterns in later stages of the migration.

1. Review the migration strategies for the portfolio

A *migration strategy* is the approach used to migrate an on-premises application to the AWS Cloud. There are seven migration strategies for moving applications to the cloud, known as the 7 Rs. Common strategies for large migrations include rehost, replatform, relocate, and retire. Refactor is not recommended for large migrations because it involves modernizing the application during the migration. This is the most complex of the migration strategies, and it can be complicated to manage for a large number of applications. Instead, we recommend rehosting, relocating, or replatforming the application and then modernizing the application after the migration is complete. For more information about the 7 Rs, see the [Guide for AWS large migrations](#).

Based on the output of the initial portfolio assessment, you have a list of all the required migration strategies for the portfolio and determined how much of the portfolio is allocated to each strategy. For example:

- Rehost - 70%
- Replatform - 20%
- Retire - 10%

2. Verify that the migration patterns for the portfolio

A *migration pattern* is a repeatable migration task that details the strategy, the destination, and the application or service used. In this step, you verify that the migration patterns include

detailed information, such as which tools to use and which AWS services are targeted. For example:

- Rehost to Amazon Elastic Compute Cloud (Amazon EC2) by using AWS Application Migration Service (AWS MGN) or Cloud Migration Factory
- Replatform to Amazon EC2 by using AWS CloudFormation templates to build new infrastructure in the AWS Cloud
- Replatform to Amazon Relational Database Service (Amazon RDS) by using AWS Database Migration Service (AWS DMS) or a native database technology
- In the [Portfolio playbook for AWS large migrations](#), you map each migration pattern to its migration strategy and document the results in a table like the following example.

Strategy	Pattern
Rehost	Rehost to Amazon EC2 by using Application Migration Service or Cloud Migration Factory
Replatform	Replatform to Amazon RDS by using AWS DMS or a native database technology
Replatform	Replatform to Amazon EC2 by using AWS CloudFormation templates to build new infrastructure in the AWS Cloud

Step 2: Validate the migration metadata and wave plan

In this step, you validate the source location of the migration metadata. You check that the data structure, such as the available columns in an Excel document, is suitable to hold the required metadata, and you check that all the metadata is available.

1. Validate the migration metadata for your migration patterns

Each migration pattern needs a different set of migration metadata in order to migrate the servers and apps. For example, a rehost migration to Amazon EC2 requires that you provide specifications for the target instance, such as the VPC subnet, security group, and instance type information. However, a storage migration, database migration, or replatform migration requires a different set of migration metadata. You typically define migration metadata requirements in

the portfolio assessment runbook, but you need to make sure that you have sufficient metadata to support each of your migration patterns. For more information about metadata identification and collection, see the [Portfolio playbook for AWS large migrations](#).

2. Validate the source location of the migration metadata and the wave plan

You typically document the source location of the migration metadata in your metadata management runbook. Ideally, the location acts as a single source of truth, such as a wave-planning spreadsheet. It is also possible that the metadata is still in multiple places, including the following common locations:

- Discovery tool
- Configuration management database (CMDB)
- App owner questionnaire
- Migration wave-planning spreadsheet

Validate the following for the metadata source location:

- a. Is the source catalog being maintained with locations of all metadata sources and owners?
- b. Does the source location (for example, wave-planning spreadsheet) have all the required migration metadata?
- c. Are there clear instructions for accessing each metadata source?
- d. If there is no single source, is each metadata source clearly mapped to its attributes?
- e. Is there a clear wave plan for the servers and apps, and are at least five waves ready for the migration workstream?
- f. Is there a process to update the sources? If so, what is the frequency and notification process?

Task exit criteria

When you have met the following exit criteria, proceed to the next task:

- You have validated the list of clearly defined migration patterns.
- The source location of the migration metadata has all the required metadata for each pattern, or a process is in place to capture any missing metadata.
- You have validated the wave plan and migration metadata for at least five waves, and you have defined a process for notifications and updates.

Task 2: Creating drafts of the migration runbooks

In this task, you draft and review migration runbooks for each migration pattern. For example, you draft a migration runbook for rehost to Amazon EC2 and another runbook for replatform to Amazon RDS. You repeat this task until you have drafted a migration runbook for every migration pattern identified in the previous task.

You can use the attached runbook templates and customize them for your environment. For migration patterns that are repeated frequently, we recommend using the *Rehost migration runbook template* (Microsoft Word format), and for patterns that are one-off or very simple, we recommend the *Rehost migration task list template* (Microsoft Excel format). You can also use a task list to track the status of tasks that are documented in a runbook. For more information, see [About the runbooks, tools, and templates](#).

This task consists of the following steps:

- [Step 1: Create a migration runbook draft for each pattern](#)
- [Step 2: Update the migration runbooks with your policies and processes](#)

Step 1: Create a migration runbook draft for each pattern

In this step, you draft runbooks for each of your migration patterns. A complete migration runbook typically contains instructions for how to use the selected migration service or tool, any tasks that are unique to your environment, and cutover instructions.

1. Open the attached *Rehost migration runbook template* (Microsoft Word format).
2. Update the *Premigration tasks* section, *Migration tasks* section, and *Cutover tasks* section with instructions that are specific to your migration pattern. Depending on your use case, you might need to update all three sections. Include the following when customizing your tasks:
 - **Standard migration instructions for the selected service** – You can typically find the information needed to complete your template in [AWS documentation](#). For example, see the following:
 - [How to use the new AWS Application Migration Service for lift-and-shift migrations](#)
 - [Getting started with AWS DataSync](#)
 - [AWS Database Migration Service step-by-step walkthroughs](#)

- **Tasks that are unique to your IT environment** – Record the tasks that are unique to your IT operations and environment. The goal is that a new person joining your migration teams can follow the runbook with minimal learning curve. For example, what monitoring software do you need to install on the target machine after cutover? Which Domain Name System (DNS) server do you use for that subnet? How do you submit a request for change (RFC)?
- **Cutover tasks** – Every environment has a slightly different cutover process. It is important to document all the steps for cutover in your environment because you want everyone to follow the same process. Documenting these steps minimizes time spent in the cutover window and helps you plan the amount of time needed to complete the cutover.

Step 2: Update the migration runbooks with your policies and processes

Runbook and task list templates cover the majority of the migration tasks, or the portion of the process that is standard. The remaining tasks are unique to your environment, and you must customize the runbook accordingly. For example, consider whether your runbooks should contain custom tasks for the following processes in your environment.

Connectivity

- How to connect to a VMware environment
- How to connect to a DNS server and update DNS records
- How to connect to the migration automation server
- How to connect to the source environment
- How to connect to a document repository, such as SharePoint or Confluence

Permissions and change management

- How to submit an RFC in your environment
- How to review the status of the RFC for each wave
- How to grant access for a new migration engineer
- How to request permissions to the source servers
- How to request permissions to the target AWS account
- Who has permission to connect to the target server after the cutover

Migration implementation and cutover

- Which software to install or uninstall on the target server
- How to change infrastructure settings, such as firewall, routing, and load balancer settings
- Who can change infrastructure settings
- How to change the application configuration during cutover
- How to conduct application testing
- How to complete a cutover and go-live
- How to complete tasks that occur after cutover, such as configuring monitoring or backups

Some of these tasks might sound trivial, but knowledge and permissions vary in any environment. It is important to document these tasks in the same migration runbook.

Tip

We highly recommend using automation to accelerate your large migration. Using a migration factory model simplifies and reduces the number of issues with repetitive tasks, especially for rehost and replatform migration patterns. [AWS Cloud Migration Factory Solution](#) was designed to help customers migrate at scale with automation. You can deploy the solution and use predefined automation scripts in your runbook.

Task exit criteria

Repeat this task as necessary, and when you have met the following exit criteria, proceed to the next task:

- You have drafted a runbook for each migration pattern.
- Each runbook draft contains three main sections: pre-migration tasks, migration tasks, and cutover tasks.
- Your runbook drafts include tasks that are unique to your environment.
- Your detailed runbook drafts include step-by-step guidance and screenshots.

Task 3: Analyzing and testing your migration runbooks

In this task, you walk through each runbook that you built in the previous task, analyze any identified gaps, conduct a migration proof of concept (POC), and review the notes and feedback.

This task consists of the following steps:

- [Step 1: Conduct a walkthrough of each runbook](#)
- [Step 2: Conduct a POC that tests each migration pattern](#)
- [Step 3: Review and identify the gaps in the current migration runbook drafts](#)

Step 1: Conduct a walkthrough of each runbook

In this step, the migration teams assess the runbook and task sequence as though they were performing it for real. The migration teams meet and review each step, and the team members ask questions and share their feedback. This walkthrough process helps the teams identify missing steps and sequence issues. Complete the walkthrough as follows:

1. Gather the migration teams that are responsible for completing the tasks in the runbook.
2. Walk through the steps in the runbook one by one, as if this was a live migration. As you go, identify and make note of any gaps or issues. Do not perform the migration or tasks as part of the walkthrough.
3. Update the runbook draft to address any gaps or issues identified in the walkthrough.

Step 2: Conduct a POC that tests each migration pattern

1. Select a POC candidate from the already prepared waves.
2. Open the migration runbook draft.
3. Complete the runbook step by step in order to migrate the POC candidate as follows:
 - Follow every step in the runbook. Do not make assumptions or make your own decisions.
 - Assume the person using the runbook has no prior knowledge about migration or your environment.
 - If a step is not clear but you can continue, make note of the step and continue.

- If a step is missing and you can't continue, stop, and highlight the section from which you could not proceed. Work with the runbook owner to clarify the missing step so that you can continue and complete the POC.

Step 3: Review and identify the gaps in the current migration runbook drafts

1. Review any issues or gaps identified in the previous steps.
2. Analyze the gaps and consider the following questions:
 - Does the runbook have the steps needed to complete a migration and cutover, from end to end?
 - Does the runbook contain reference links for the tasks that are predefined in your environment?
 - Does the runbook clearly defined who, what, when, and how to complete a task?

Task exit criteria

When you have met the following exit criteria, proceed to the next task:

- You have reviewed and tested each migration runbook.
- For each runbook, you have completed a migration POC for at least one application and for more than two operating system (OS) variants.
- You have identified and documented the identified gaps and issues in each runbook.

Task 4: Improving your migration runbooks

In this task, you improve the runbooks by repeating the POC multiple times. With each wave, the POC test and *retrospective*, a meeting in which the team reviews the completed wave, provide opportunity to improve the runbooks. You also improve your runbooks by automating repetitive tasks, which increases the velocity of the migration and reduces the risk of manual configuration errors.

This task consists of the following steps:

- [Step 1: Update the migration runbooks and repeat the testing](#)

- [Step 2: Automate repetitive tasks](#)
- [Step 3: Build a migration task list](#)

Step 1: Update the migration runbooks and repeat the testing

1. For the issues and gaps identified in the previous task, update the runbooks with detailed instructions. For example:
 - If a step is missing, add step-by-step instructions
 - If a step is not clear, consider updating the text, adding a screenshot, or adding reference links
2. Repeat the previous task until you are satisfied that the instructions are complete and clear.
3. Test the final draft of each runbook by asking a new migration team member, one who has not tested this runbook before, to perform a POC and complete the runbook.

Step 2: Automate repetitive tasks

1. Review each runbook and identify areas of automation for manual tasks. Consider the following probing questions:
 - Are there any repetitive, manual tasks for each server or app in the runbook?
 - Are there any actions that you perform on every server or application?
 - Do you need to install or uninstall software on the target server?
 - Do you need to change network or infrastructure settings one by one for each server?
 - Do you need to manually copy and paste any data?
2. Build automation scripts and update the runbooks.
3. Repeat task 3 and task 4 until you have documented the runbooks with clear and complete information and automated repetitive migration tasks.

Note

For automating migration tasks, we highly recommend that you build new scripts or customize existing scripts in [AWS Cloud Migration Factory Solution](#).

Step 3: Build a migration task list

A migration task list can help you manage the status and owners of tasks. You build a task list for each migration runbook, and you include the high-level information from the runbook without including the details. A task list typically contains the following information, and you can add more attributes as needed:

- Descriptive name, such as:
 - Check server OS version
 - Install an agent
 - Restart a server
 - Update the DNS
- Dependencies
- Sequence of tasks
- Owner
- Estimation of time required to complete each task
- Status

There are many tools available for creating and managing task lists. You can use the attached *Rehost migration task list template* (Microsoft Excel format). You can also use project management tools, such as Jira or a Kanban board.

Note

We also recommend using the Excel task list template to document small, well-understood, or non-repetitive tasks, such as restarting a server or getting an IP address. These tasks should be captured and tracked but don't require the detailed steps of the Word runbook template.

Task exit criteria

Repeat this task as necessary, and when you have met the following exit criteria, proceed to the next task:

- You have identified opportunities for automation and have either developed automation scripts or have a plan to do so.
- Three or more people have peer-reviewed each runbook.
- Two or more people who were not on the development team for the runbook have tested it end-to-end.
- Using the most up-to-date runbook, you have migrated 20 or more servers to more than one AWS account.
- You have developed a task list to help track and manage the progress of the migration.

Stage 2: Implementing a large migration

In stage 1, you developed migration runbooks for each migration pattern. In stage 2, you use these runbooks to migrate servers and then improve the runbooks in order to accelerate the velocity of the migration. Building and updating runbooks is not a one-off task. You might need to do that throughout your large migration journey. For example, you might need to create new runbooks if the scope increases and you identify new migration patterns, or you might need to improve the existing runbooks if the migration velocity is below the target and introducing more automation would reduce the number of manual tasks and accelerate the migration.

Note

The wave plan developed in the portfolio workstream determines the activities in the migration workstream. Before starting stage 2, verify that you have validated your wave plan. For instructions and more information about the wave plan, see [Portfolio playbook for AWS large migrations](#).

Stage 2 consists of the following tasks and steps:

- [Task 1: Performing sprint planning for scheduled waves](#)
 - [Step 1: Review the backlog for the scheduled waves](#)
 - [Step 2: Assign tasks and establish due dates](#)
- [Task 2: Performing migration tasks](#)
- [Task 3: Performing cutover tasks](#)
- [Task 4: Reviewing and improving the migration runbooks](#)
 - [Step 1: Review the completed waves and identify gaps in the current migration runbook](#)
 - [Step 2: Update the migration runbooks and complete testing](#)

Task 1: Performing sprint planning for scheduled waves

In this task, you assign waves to *sprints*, which is a fixed period of time in which the migration team works on all waves within that sprint. If each sprint is 2 weeks in duration, each wave spans at least two sprints. *Sprint planning* refers to the process of assigning owners and due dates to all of the tasks within that sprint.

This task consists of the following steps:

- [Step 1: Review the backlog for the scheduled waves](#)
- [Step 2: Assign tasks and establish due dates](#)

Step 1: Review the backlog for the scheduled waves

In this step, you review existing *backlogs*, or current and pending tasks, for all the concurrent waves, and you use the recommended tools and mechanisms to manage the wave. For example, you might use a Kanban board with a swimlane for each wave, or you might use Jira and track waves with stories and epics. For more information, refer to the [Project governance playbook for AWS large migrations](#).

Step 2: Assign tasks and establish due dates

In this step, for all waves in this sprint, you assign owners to each task and set a due date accordingly. You can use the migration task list spreadsheet you created in stage 1 to manage your wave progress, task ownership, and due dates, and the tasks are defined in detail in the migration runbook for each pattern. Because waves typically overlap, it is common to manage many concurrent tasks from different waves at the same time. In addition, each wave can range from 3-6 weeks, depending on your internal process. For an example of a wave schedule, see the [Stage 2: Implement a large migration](#) section of the *Guide for AWS large migrations*.

Important

Do not add tasks to the sprint without updating the runbook or task list. These documents that you built in stage 1 should be a source of truth for all your migration activities. If any step is missing or incorrect, update and validate the runbook before adding tasks to the sprint.

Task 2: Performing pre-migration and migration tasks

Now you perform pre-migration and migration tasks and adhere to a schedule based on your sprint planning outcome. A sprint backlog contains a list of all tasks in the migration, for all waves in the current sprint, and organizes the tasks by week. For a list of tasks, see your migration runbooks for each migration pattern, which were created in stage 1 of this playbook. For the wave schedule, see

your project management tools, which were established in the [Project governance playbook for AWS large migrations](#). Perform the tasks in the scheduled weeks. The following is an example of a rehost migration task schedule in which there are migration tasks for different waves in the same week.

Task name	Wave	Category	Owner
Verify prerequisites	Wave 1	Build	Jane Doe
Install replication agent	Wave 1	Build	Jane Doe
Validate launch template	Wave 2	Validate	Jane Doe
Launch test instances	Wave 3	Boot-up testing	Jane Doe

Task 3: Performing cutover tasks

At this point, you have completed the migration tasks and tested all of the servers and apps, and you are ready for cutover. Use the RACI matrices you created in the [Foundation playbook for AWS large migrations](#) to manage the tasks and ownership of each cutover task, and use your migration runbook for each pattern to perform the cutover activities. The following table is an example of how you might track and manage cutover progress. It is common to have multiple migration patterns in the same wave for different applications.

Task name	Wave	Migration runbook	Owner	Status
Check replication	Wave 1	Rehost to Amazon EC2	Jane Doe	Completed
Launch cutover EC2 instance	Wave 1	Rehost to Amazon EC2	Jane Doe	Completed
Validate EC2 instance status	Wave 1	Rehost to Amazon EC2	Jane Doe	In progress

Launch databases in Amazon RDS	Wave 1	Replatform to Amazon RDS	John Smith	In progress
Complete storage data transfer	Wave 1	Replatform to Amazon Elastic File System (Amazon EFS)	John Smith	Not started
Perform app testing	Wave 1	All	Jane Doe	Not started
App acceptance decision	Wave 1	All	Jane Doe	Not started

Task 4: Reviewing and improving the migration runbooks

This task consists of the following steps:

- [Step 1: Review the completed waves and identify gaps in the current migration runbook](#)
- [Step 2: Update the migration runbooks and complete testing](#)

Step 1: Review the completed waves and identify gaps in the current migration runbook

Fail fast is a philosophy that uses frequent and incremental testing to reduce the development lifecycle, and it is a critical part of an agile approach to a large migration. After each cutover, schedule a retrospective meeting to review each task with the migration teams. Ask the following probing sample questions. You can also add your own questions:

- Was the cutover successful? If not, what was the issue?
- Does the migration runbook cover all of the tasks to perform the migration and cutover?
- Do any of the tasks take longer than expected?
- Are you aware of any technical issues with any tasks in the runbook?
- Are there any manual tasks that can be automated?

- Are there any process-related issues with the runbook or cutover?

Step 2: Update the migration runbooks and complete testing

After collecting data from the retrospective meeting, update the migration runbooks as follows:

- Add detailed instructions for any missing steps.
- Fix or update any steps as needed.
- Perform an end-to-end migration test with at least one Windows and one Linux server.
- Send the updated runbook to the migration teams for use in the next wave.

Resources

AWS large migrations

To access the complete AWS Prescriptive Guidance series for large migrations, see [Large migrations to the AWS Cloud](#).

Additional references

- [AWS Cloud Migration Factory Solution](#)
- [AWS Prescriptive Guidance migration patterns](#)

Contributors

The following individuals contributed to this document:

- Chris Baker, Senior Migration Consultant
- Wally Lu, Principal Consultant

Document history

The following table describes significant changes to this guide.

Change	Description	Date
Updated name of AWS solution	We updated the name of the referenced AWS solution from <i>CloudEndure Migration Factory</i> to <i>Cloud Migration Factory</i> .	May 2, 2022
Initial publication	—	February 28, 2022
